



THE PLAN

The plan: your first 90 days

What you do each week from Monday 14 September to Saturday 12 December 2026, and the four decisions that control it.

Status labels apply throughout: KNOWN, VERIFIED, ASSUMPTION, ESTIMATE, TO VALIDATE, PROPOSED. Nothing in this document claims traction, approvals, partners or revenue that do not exist. Governing file: FACTS_BASE.

PREPARED FOR

The Founder, Vytalix

DATE

8 September 2026

VERSION

1.0 · Confidential draft

What you do each week from Monday 14 September to Saturday 12 December 2026, and the four decisions that control it.

In one minute

- Ninety days to turn an idea into a real company that trades and tells the truth.
- Four blocks: fix the basics, build the sales engine, meet investors, launch.
- Four decisions control everything: the company, the ownership, MaternaLink, Ekiti.
- Money comes first. One paying client by 13 October, three by 12 December.
- You speak to no investor until the first three decisions are closed.


What to do

Action	Who	By when
Open the four blockers: name check, company decision, ownership talk, old claims withdrawn	You	Mon 14 Sept 2026
Get the standstill letter signed and send the first 40 sales messages	You	Fri 18 Sept 2026
Register the company	You and the accountant	Fri 25 Sept 2026
First signed client, and the ownership deed signed	You and the solicitor	Tue 13 Oct 2026
Decide Ekiti, then decide whether to build MaternaLink	You, with the board	Thu 12 Nov and Tue 8 Dec 2026

The ninety days at a glance

The first 90 days

Four blocks. Do them in order. Dates run from Monday 14 September 2026.

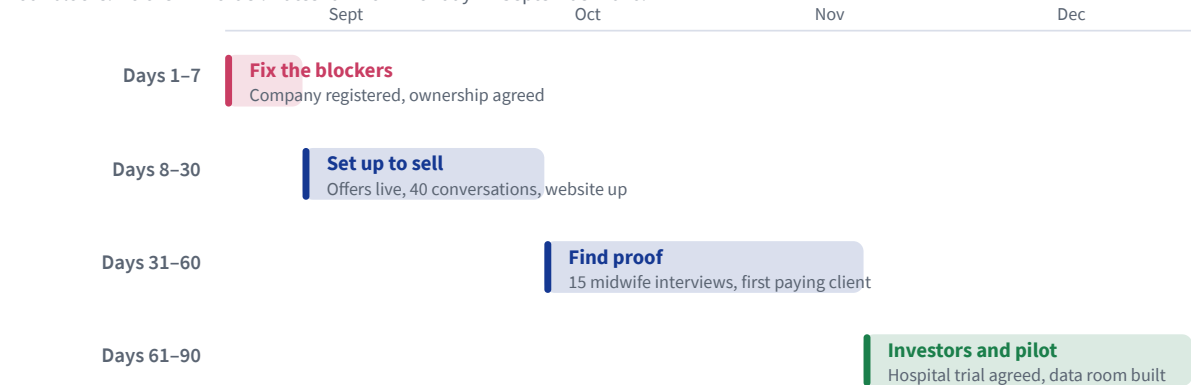

Fix the basics first; everything else waits behind those seven days.

Week one, day by day

Day one is Monday 14 September 2026.

Day	What you do	Why	What you end up with
Mon 14 Sept	Set your weekly rhythm and your two trackers. Run the name and trademark checks on "Vytalix" and "MaternaLink" at Companies House, UK IPO, EUIPO and USPTO. Decide to register one English company. Send David Agunede a meeting request with your written questions and the ownership questionnaire. Write down that the 2025 AI deck and the £36m Ekiti headline are withdrawn from all outside use.	Every later step needs a name, a company and a clear owner. Nothing you say in public is safe until the old claims are gone.	Two decisions logged, search results saved with dates, a meeting booked for Wednesday, the old deck withdrawn
Tue 15 Sept	Set up the free CRM (the software that holds your contacts and deals). Build the first 50 of a 150-name list. Rewrite your LinkedIn profile so it says "pre-seed" and "in development". Publish your first post. Ask three solicitors and three accountants to quote.	You cannot sell without a list, and you cannot sign anything without a solicitor.	CRM live, 50 named contacts with sources, an honest profile, six quotes coming
Wed 16 Sept	Hold the ownership conversation with David Agunede, one hour, notes written the same day. Establish who wrote the code and the decks, who pays for the prototype, whether real patient data was ever entered, and what happened after the 18 March 2026 Ekiti email. Hand him the 60-day standstill letter. Adopt the new MaternaLink description: it helps midwives coordinate care, it does not diagnose. Take the old claims out of every file.	Undocumented ownership and over-claiming are the two things that end an investor call in minutes.	A written note of the facts, the letter with him for signature, the new product wording adopted, zero old claims left
Thu 17 Sept	Take the trademark attorney's opinion call on "Vytalix". Choose the solicitor and send the instruction. Send the standstill letter for signature. Send the first 20 sales messages. Publish your third post.	Tomorrow's name decision needs a professional opinion, not your guess. The first client is due on day 30, so selling starts now.	Attorney memo requested, solicitor engaged, 20 messages logged
Fri 18 Sept	Decide the name. If the checks are clean, use it; if not, use the reserve name rather than wait. Buy the domain and set up email. Sign both engagement letters. Get the standstill signed. Send messages 21 to 40. Log how much cash you have. Hold your first Friday review.	A cleared name and a professional bench are what week two is built on.	Name decision, domain and email, two engagement letters, a signed standstill, 40 messages sent, a 13-week cash plan

Weekend: read the draft ownership terms on Saturday, send them to David Agunede on Sunday 20 September.

Weeks two to four

Week	What you do	What you end up with
Week 2, 21 to 27 Sept	File the incorporation (target Wed 23, hard deadline Fri 25). Sign your own IP assignment the same day. Send contract templates to the solicitor. Get insurance quotes. Apply for the bank account. Hold your first two discovery calls and send proposal one. Start the prototype audit.	A registered company, a bank application in, first buyer feedback
Week 3, 28 Sept to 4 Oct	Full sales quota begins: 40 contacts, 20 conversations, 5 discovery calls, 2 proposals each week. Register with the ICO. Bind the insurance. Open the bank account. Start the SEIS and EIS paperwork. Draft the grant calendar and the data room list. Build the 30-name list for UK interviews.	Insured, registered, banked, and selling at full rate
Week 4, 5 to 11 Oct	Adopt the new pricing memo, so the £300 per woman per year figure is gone from every document. Ask for the Ekiti status call and hold it. Approach the first three advisers. Publish the website. Send newsletter one. Negotiate the first engagement.	Website live, honest pricing, Ekiti facts known, data room version one
Days 29 to 30, 12 to 13 Oct	Sign the first client and raise the invoice. Execute the ownership deed. Receive the prototype audit report. Submit the SEIS and EIS application. Hold the first board meeting.	Revenue exists, ownership is documented, phase two is closed

Days 31 to 60

Fortnight	What you do	What you end up with
Days 31 to 45, 14 to 28 Oct	Check that the company, the ownership and the claims are all closed; only then start investor outreach. Contact the top 25 investors, phone first. Decide whether to bid for a grant (by Fri 23 Oct). File the trademark (Wed 28 Oct). Identify a Clinical Safety Officer. Keep the sales quota. Run UK interviews.	25 investors contacted, trademark filed, first meetings booked
Days 46 to 60, 29 Oct to 12 Nov	Contact the next 50 investors. Hold the mDoc conversation and score two other Nigerian states. Decide Ekiti (Thu 12 Nov). Sign two advisers and engage the Clinical Safety Officer. Complete 15 UK interviews and draft the research report. Sign the second client.	75 investors contacted, 4 meetings, Ekiti decided, second client signed

Days 61 to 90

Fortnight	What you do	What you end up with
Days 61 to 75, 13 to 27 Nov	Publish the research report (Fri 20 Nov) and run the webinar (Tue 17 Nov). Start on the next 75 investors. Act on the Ekiti decision by Fri 27 Nov. Keep second meetings moving with 48-hour answers.	Report published, webinar delivered, Nigeria path chosen
Days 76 to 90, 28 Nov to 12 Dec	Sign the third client. Make the MaternaLink build decision (Tue 8 Dec): build, build small, or wait. Get Cyber Essentials certified. Hold the fourth adviser meeting and the third board meeting. Write the plan for the next quarter (Sat 12 Dec).	Three clients, £15k to £30k contracted (ESTIMATE, our best guess), a minuted product decision, a Q1 plan

Four decisions you must make

Decision	Decide by	If yes	If no
Register the company	Decide Mon 14 Sept; filed by Fri 25 Sept	You can invoice, insure, bank, and apply for tax relief and grants	Every later item slips day for day; delay past 25 September is not acceptable
Settle the ownership with David Agunede	Terms sent Sun 20 Sept; deed signed Tue 13 Oct; hard stop Thu 12 Nov	You can say Vytalix owns MaternaLink and name it to investors	Until it is signed, call it "a concept Vytalix is developing with a collaborator". If nothing is signed by 12 November, rebuild version one from scratch and drop his materials and the "Maternal Link" name
Re-scope MaternaLink	Wed 16 Sept	Version one coordinates care and does not diagnose; the AI risk score moves to a research track for later	Keeping the prediction claims needs a medical device route, data and ethics you do not have and cannot fund
Decide on Ekiti	Thu 12 Nov, after the status call, the mDoc conversation and a two-state scorecard	Offer a small, re-priced, partner-aware pilot, and only with board approval	Move to a better-scoring state with an NGO, or stop Nigerian government work for six months. The £4.5m and £300 per woman proposal is not restated under any option

How to decide anything else

Score any idea out of 100. Ten points, each marked 1 to 10.

Point	A high score means
1 Strategic fit	It matches the plan: services pay the bills, MaternaLink is the long story, UK first

Point	A high score means
2 Money	Real cash within 12 to 24 months, and a large repeat stream later
3 Demand	A named buyer has said they want it and can pay
4 Speed	First paying customer in weeks, not years
5 Cost	Cheap to reach the first result, under £2,000
6 Growth	It grows without more of your hours
7 Advantage	A real difference from named competitors that you can build in a year
8 Rules risk	Little exposure to medical device, data or clinical safety rules
9 Simplicity	One owner, known steps, no outside dependency
10 You can do it	You can deliver it alone, with the time and skills you have now

Points 5, 8 and 9 are scored backwards on purpose. Cheap, low risk and simple all score high, so a bigger total is always better.

Total	Verdict	What it means
70 or more	BUILD	Commit your time and money now; it goes in the plan with dates
50 to 69	TEST	Promising but unproven; run one bounded experiment with a budget cap and a decision date
35 to 49	WAIT	Not now; write down the trigger that brings it back
Under 35	STOP	Not pursued as stated; the idea underneath may return in a different form

Four rules beat the total. If strategic fit is 3 or less, it is STOP. If rules risk is 2 or less, WAIT is the best it can be. If you cannot do it alone and cannot pay a team, WAIT. If nobody has said they want it, it can never be BUILD.

Scores for the eight live ideas, made 8 September 2026. All are ESTIMATES (our best guess, not facts).

Idea	Score	Verdict
A. Advisory work you deliver yourself	76	BUILD
B. A research report used to attract clients	65	TEST
C. MaternaLink version one, care coordination only	59	TEST
D. Chasing an NHS pilot, starting as a design partner	54	TEST
E. Launching e-learning in year one	49	WAIT
F. White-label MaternaLink for NGOs	45	WAIT
G. The MaternaLink AI risk score as a product now	33	STOP for now (rules risk)
H. The Ekiti proposal at £300 per woman per year as written	33	STOP as written (no proven buyer)

Re-score every quarter, first in the week of Monday 14 December 2026. Any score that moves by three points or more must name the new evidence.

What not to waste time on

- Any investor conversation before the company, the ownership and the claims are settled. It is the fastest way to lose a good investor.
- Building the MaternaLink app before the decision on Tuesday 8 December. You do not yet know what to build or who pays.
- The AI risk score as a product. It needs a medical device route, a data partner and an ethics review you cannot fund this year.
- Repeating the £300 per woman per year figure or the £36m Ekiti number. Both are withdrawn.
- E-learning courses and white-label versions. Both are WAIT; a waiting list page is all they get.
- Paid logos, printed brand work or a fancy website before the name is cleared on Friday 18 September.
- Hiring anyone. A virtual assistant only if admin passes eight hours a week for two weeks running.

Words explained

Word	What it means
Standstill letter	A short signed promise that neither side sells, licenses or shows MaternaLink to anyone else for 60 days while you agree terms
Heads of terms	A one or two page summary of a deal, agreed before the solicitors write the full contract
Discovery call	A first 30 to 45 minute call with a possible client, to find out what they need
SEIS and EIS	Tax schemes that give people money back when they invest in a small British company
ICO	The UK office you must register with, and pay £52 a year, if you hold people's personal data
Data room	One tidy folder of documents an investor reads before deciding
Cyber Essentials	A basic UK government security certificate that buyers ask for
